

ROB at *Mulamkunnathukavu*

*Progress as on 22.04.2011*

## **PROJECT MEMBERS**

Manager in Charge (RBDCK) : Radhakrishnan V  
mob : 9447178783

Site in Charge (KITCO) : Rahul  
mob : 8891772513

Project Engineer (GPT) : Nikhil  
mob : 9539007550

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK

ROB at Mulamkunnathukavu

Progress as on 22.04.2011

Revised Progress Report For Mulamkunnathukavu ROB for the week ending on 22-04-2011												
Si No	Activity Description	Total Quantity	Cumulative progress upto last week	Balance work up to last week	Cumulative delay in Qty up to last week	Work planned during the week	Actual work done during the week	Cumulative delay in Qty up to this week	Work Planned for next week	No of days remaining for completion as per the weekly plan	Remarks	
1	PILE SHORNUR SIDE	9	9	Completed								
2	PILE M.C SIDE	36	36	Completed								
3	PILE CAP SHORNUR SIDE	3	3	Completed								
4	PILE CAP M.C SIDE	12	12	Completed								
5	PIER SHORNUR SIDE	3	3	Completed								
6	PIER M.C SIDE	12	12	Completed								
7	PIER CAP SHORNUR SIDE	3	3	Completed								
8	PIER CAP M.C SIDE	12	12	Completed								
9	RE/R WALL SHORNUR SIDE	100%	9	91%	0	10.00 %	0.00%	66.00%	10.00%	102 days		
10	RE/R WALL M.C SIDE	100%	9	91%	0	5.00%	0.00%	33.00%	5.00%	102 days		
11	BEAM/SLAB SHORNUR SIDE	3	0	3	0	0	0	0	0*	72 days		

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK

12	BEAM/SLAB M.C SIDE	12	3	9	0	1	1	1	1	132 days	concreting of 3 spans in the M.C side completed. reinforcement work and shuttering work of the girder of the fourth span P13-P12 in progress. staging work of the span P8-P7 in progress. deshuttering work of the span P9-P10 in progress
13	HR/FP/KERB SHORNUR SIDE	100%	0	100%	0	0.00%	0.00%	0.00%	0.00%	53 days	
14	HR/FP/KERB M.C SIDE	100%	3	95%	0	2.00%	2.00%	0.00%	0.00%		
15	BC/PAINTIN G	100%	0	100%	0	0.00%	0.00%	0.00%	0.00%		

## ROB at Mulamkunnathukavu

Progress as on 22.04.2011

Availability of Men						
Date	16-4-'11	17-4-2011	18-4-2011	19-4-2011	20-4-2011	21-4-2011
Nof labours	20	Holiday	20	20	20	25

### Material Stocking Status

	Required	Available	Remarks
Fine aggregate {cft}	100	500	
Cement(bag)	630	770	
			sufficient material available at the site
Steel inT	11	18	
Coarse Aggreagate (cft)	400	600	

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK

## ROB at Mulamkunnathukavu


Progress as on 22.04.2011

Utility shifting		
Utilities to be shifted		Remarks
BSNL	hindrance	talked to the BSNL in charge of the locality.agreement made to re-route the cable.
KSEB	already shifted	
KWA	hindrance	given the letter to the AE and AXE of the water authority, thrissur, to visit the site and take the estimate of the rerouting cost as soon as possible. The hindrance is in the west side of canal. (Pipe line shifted as on 23.04.2011)
Others	WBM completed, BM to be started	
	canal diversion work will be started after 30th of this month.	
	THE WATER AUTHORITY HAS STARTED THE TRANCHING WORK FOR THE PIPE LINE SHIFTING.THE BSNL AUTHORITIES INFORMED THEY WILL RE-ROUTE THE CABLES AFTER THE TRENCHING WORK FOR THE KWA PIPELINE.	
	THE CANAL WORK CANNOT BE STARTED AS THE CANAL IS FILLED WITH WATER.	

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK

## Progress Graph

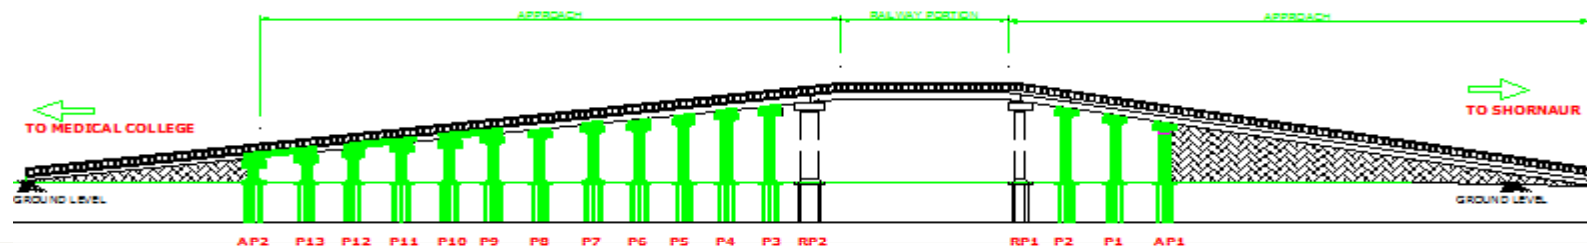

- CUMULATIVE WORK COMPLETED TILL LAST WEEK
- CUMULATIVE DELAY TILL LAST WEEK
- WORK COMPLETED IN THE WEEK
- DELAY OF WORK IN THE WEEK
- WORK SCHEDULED IN THE WEEK  +

**MULAMKUNNATHUKAVU  
LC NO. 14 (KM.23/5-6)**

Status as on :22-04-2011



## **Progress between 09.04.2011 to 15.04.2011**

- 1) Concreting of beam and slab P9-P10 completed.
- 2) Staging and barbending work of fourth span P12-P13 is in progress.
- 3) Staging work of fifth span P8-P7 is in progress.

ROB at *Mulamkunnathukavu*

*Progress as on 22.04.2011*



Deshuttering of span P9-P10 - 16.04.2011

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK



ROB at *Mulamkunnathukavu*

*Progress as on 22.04.2011*



Reinforcement work for slab P13-P12 - 18.04.2011

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK



Reinforcement work for pedestal - 19.04.2011

ROB at *Mulamkunnathukavu*

*Progress as on 22.04.2011*



Staging work for 5th span - 19.04.2011

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK

ROB at *Mulamkunnathukavu*

*Progress as on 22.04.2011*



Earth work excavation for shifting water supply pipeline - 20.04.2011

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK

ROB at *Mulamkunnathukavu*

*Progress as on 22.04.2011*



shuttering and barbending work of span P13-P12 -20.04.2011

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK

ROB at *Mulamkunnathukavu*

*Progress as on 22.04.2011*



Shuttering and barbending work of P13-P12 - 21.04.2011

Site Engineer : Rahul (8891772513)  
KITCO

Manager in charge :Radhakrishnan V (9447178783)  
RBDCK

**LABOUR ATTENDANCE FOR ROB MULAMKUNNATHUKAVU SITE**

Date	Barbender/Carpenter	Welder	Operators	Labours	Total
16/04/2011	2	1	3	14	20
17/04/2011	2	1	3	14	20
18/04/2011	2	1	3	14	20
19/04/2011	2	1	3	14	20
20/04/2011	2	1	3	14	20
21/04/2011	2	1	3	19	25

**Thank  
You**
